RED LAKE CONSTRUCTION CO. LTD.
BUILDERS - CONTRACTORS - DEVELOPERS - PROJECT MANAGERS

Ecole Dugald School

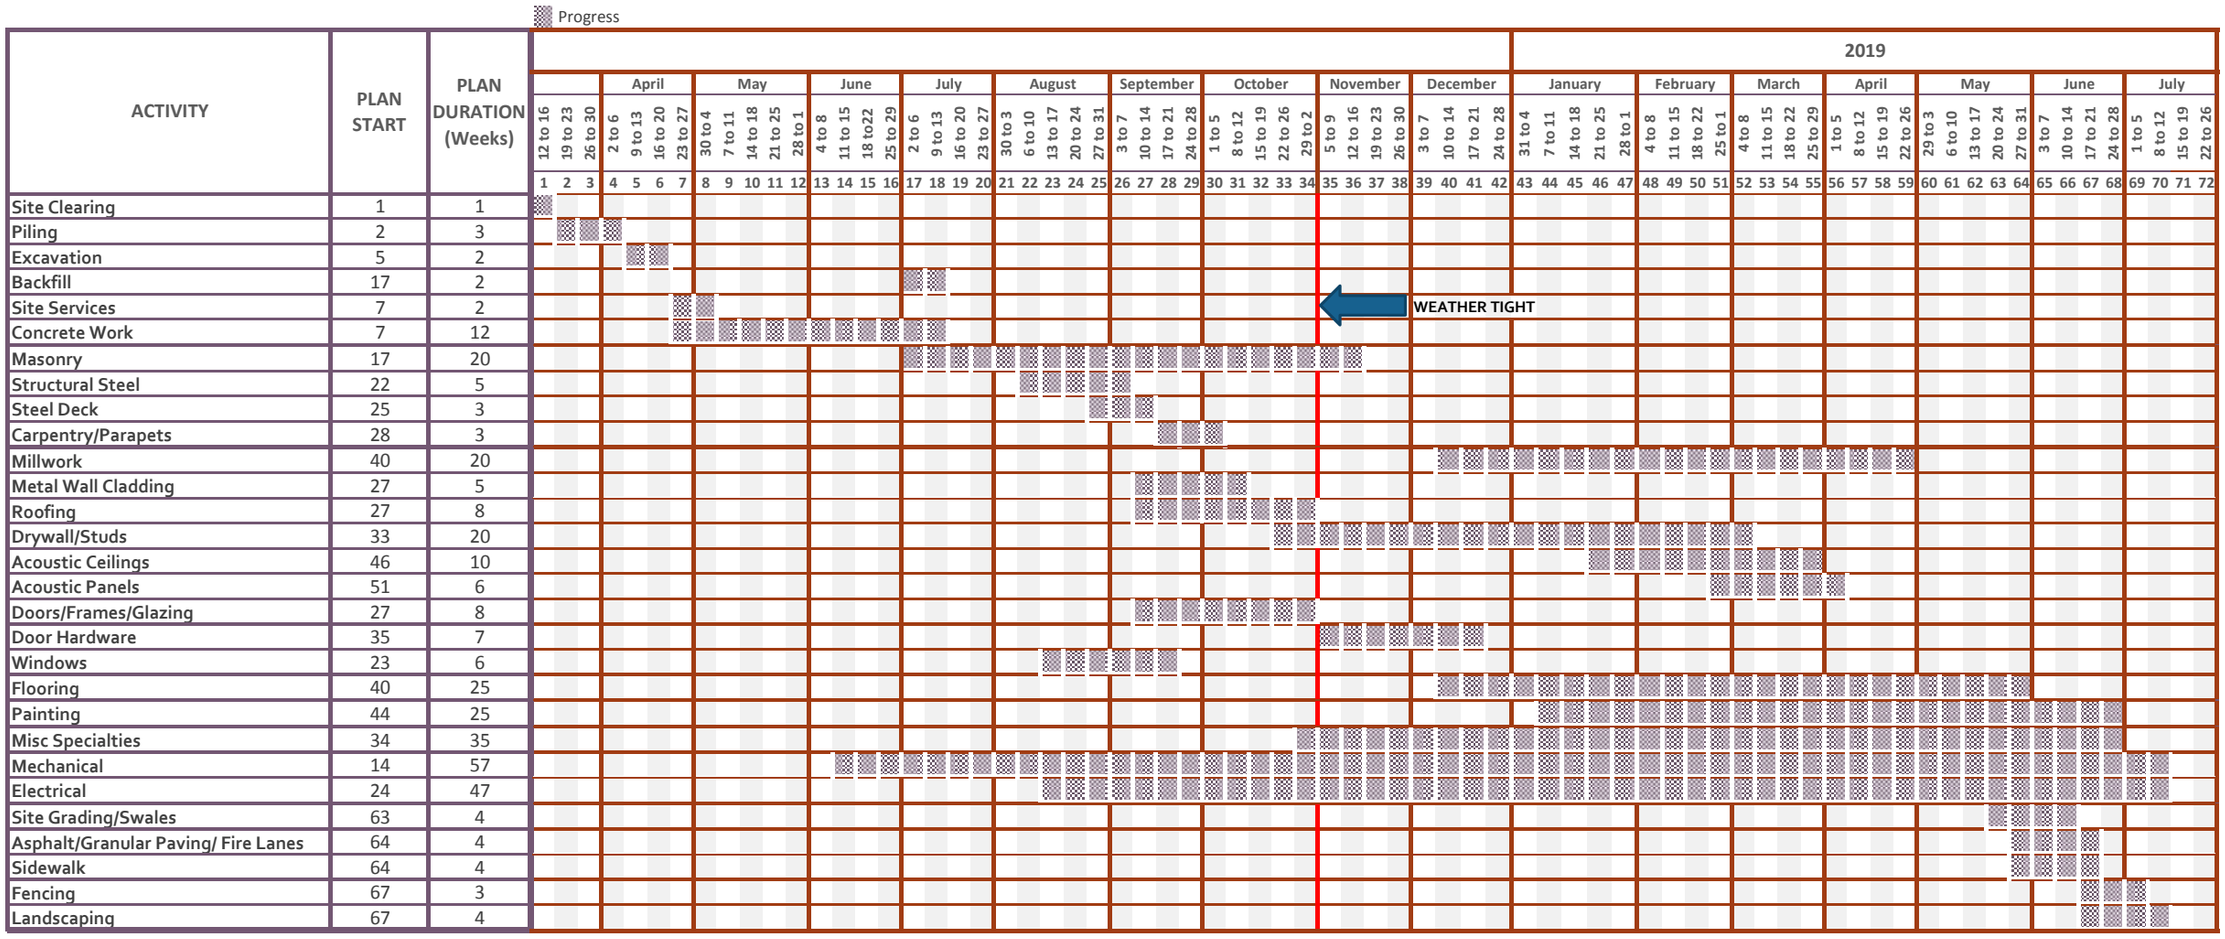

ACTIVITY	PLAN START	PLAN DURATION (Weeks)
Site Clearing	1	1
Piling	2	3
Excavation	5	2
Backfill	17	2
Site Services	7	2
Concrete Work	7	12
Masonry	17	20
Structural Steel	22	5
Steel Deck	25	3
Carpentry/Parapets	28	3
Millwork	40	20
Metal Wall Cladding	27	5
Roofing	27	8
Drywall/Studs	33	20
Acoustic Ceilings	46	10
Acoustic Panels	51	6
Doors/Frames/Glazing	27	8
Door Hardware	35	7
Windows	23	6
Flooring	40	25
Painting	44	25
Misc Specialties	34	35
Mechanical	14	57
Electrical	24	47
Site Grading/Swales	63	4
Asphalt/Granular Paving/ Fire Lanes	64	4
Sidewalk	64	4
Fencing	67	3
Landscaping	67	4
